

PROGRESS

Foundation	72 / 141
Erection	62 / 141
Earthing	59 / 141
Stringing	0.100 km / 15.709 km

132 kV S/C Rilo - Sagali TL


KEC INTERNATIONAL LTD.

Page 1 / 4 (Locations: AP 1 to AP23)

Progress data as on Wednesday, April 8, 2026

LEGEND

Crossings		Status	
	Road Crossing		Completed
	Rail Crossing		In Progress
	River Crossing		Right of Way
	Powerline Crossing		Planned
	Forest Crossing		Earthing Done

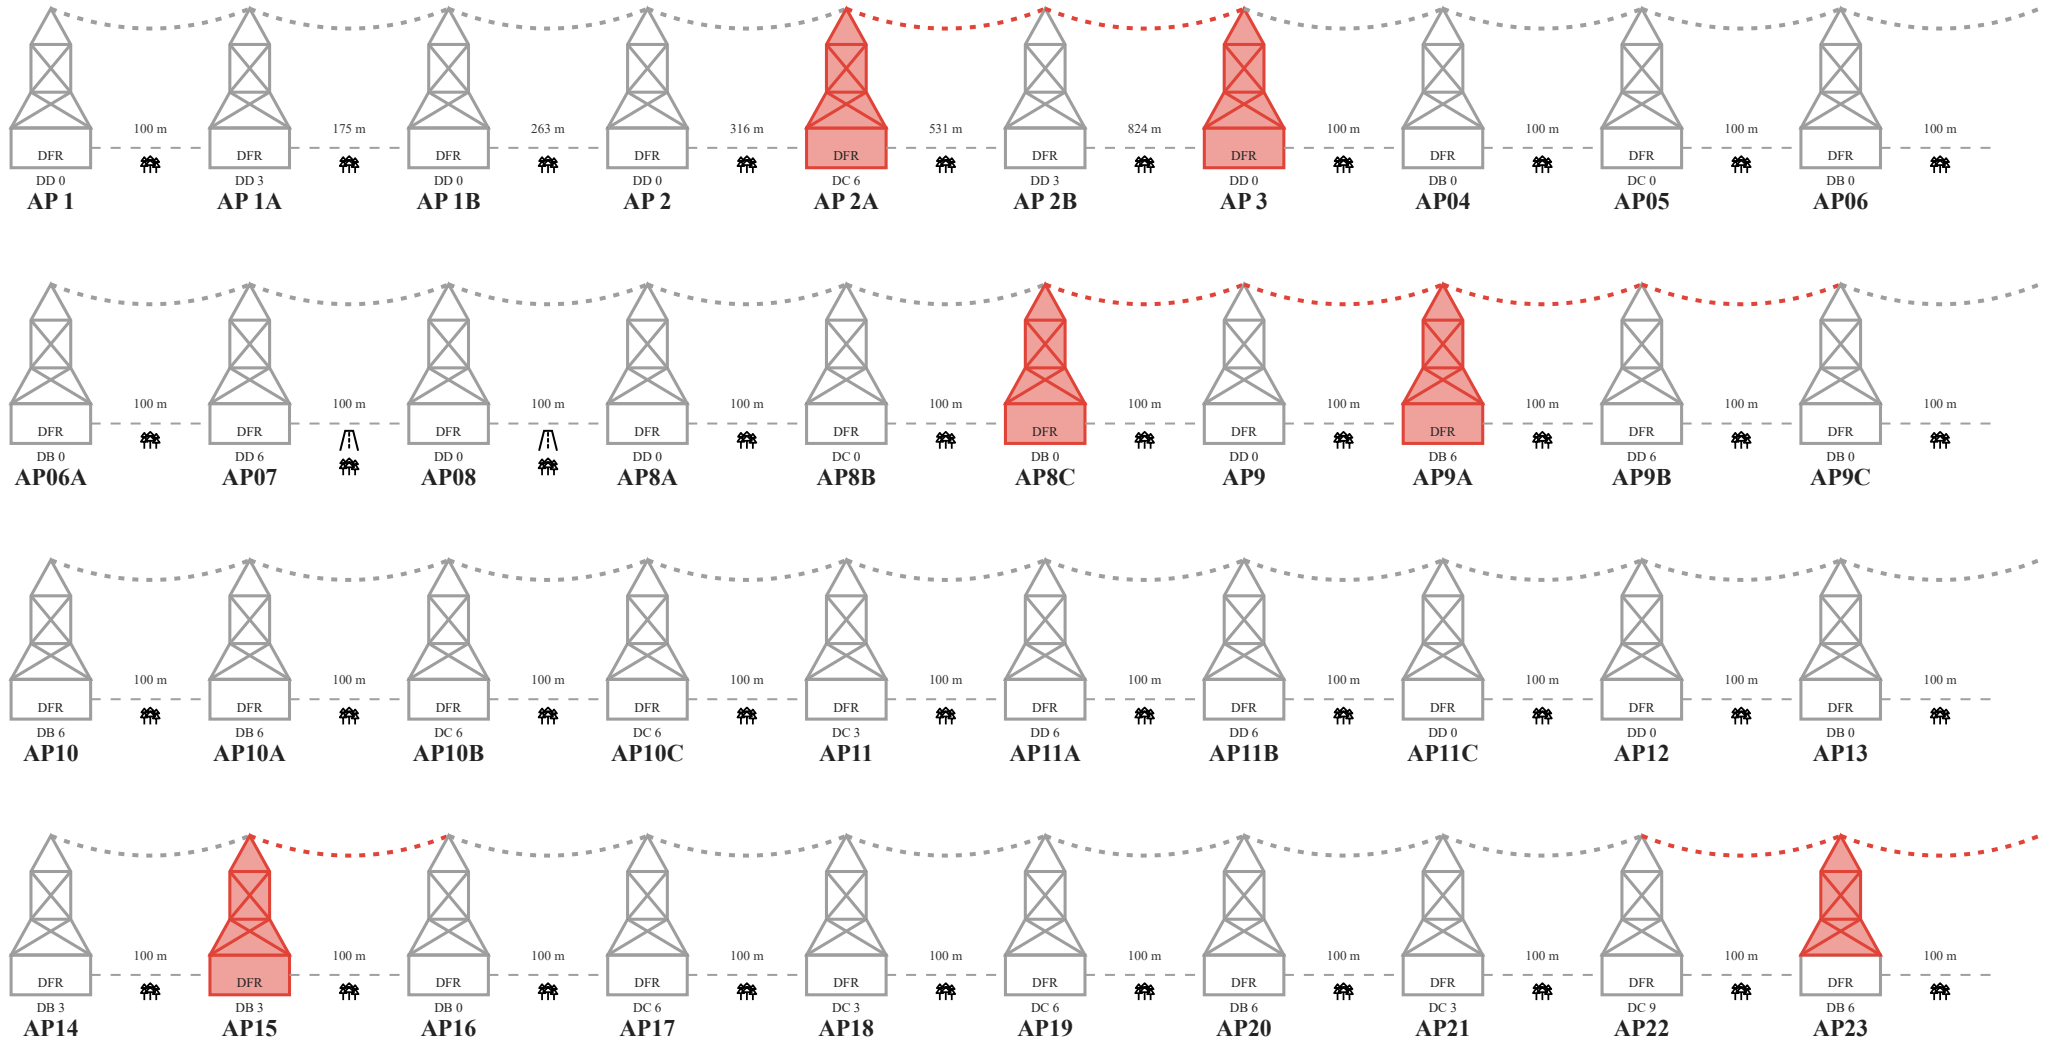

PROGRESS

Foundation	72 / 141
Erection	62 / 141
Earthing	59 / 141
Stringing	0.100 km / 15.709 km

132 kV S/C Rilo - Sagali TL


KEC INTERNATIONAL LTD.

Page 2 / 4 (Locations: AP24 to AP59)

Progress data as on Wednesday, April 8, 2026

LEGEND

Crossings		Status	
	Road Crossing		Completed
	Rail Crossing		In Progress
	River Crossing		Right of Way
	Powerline Crossing		Planned
	Forest Crossing		Earthing Done

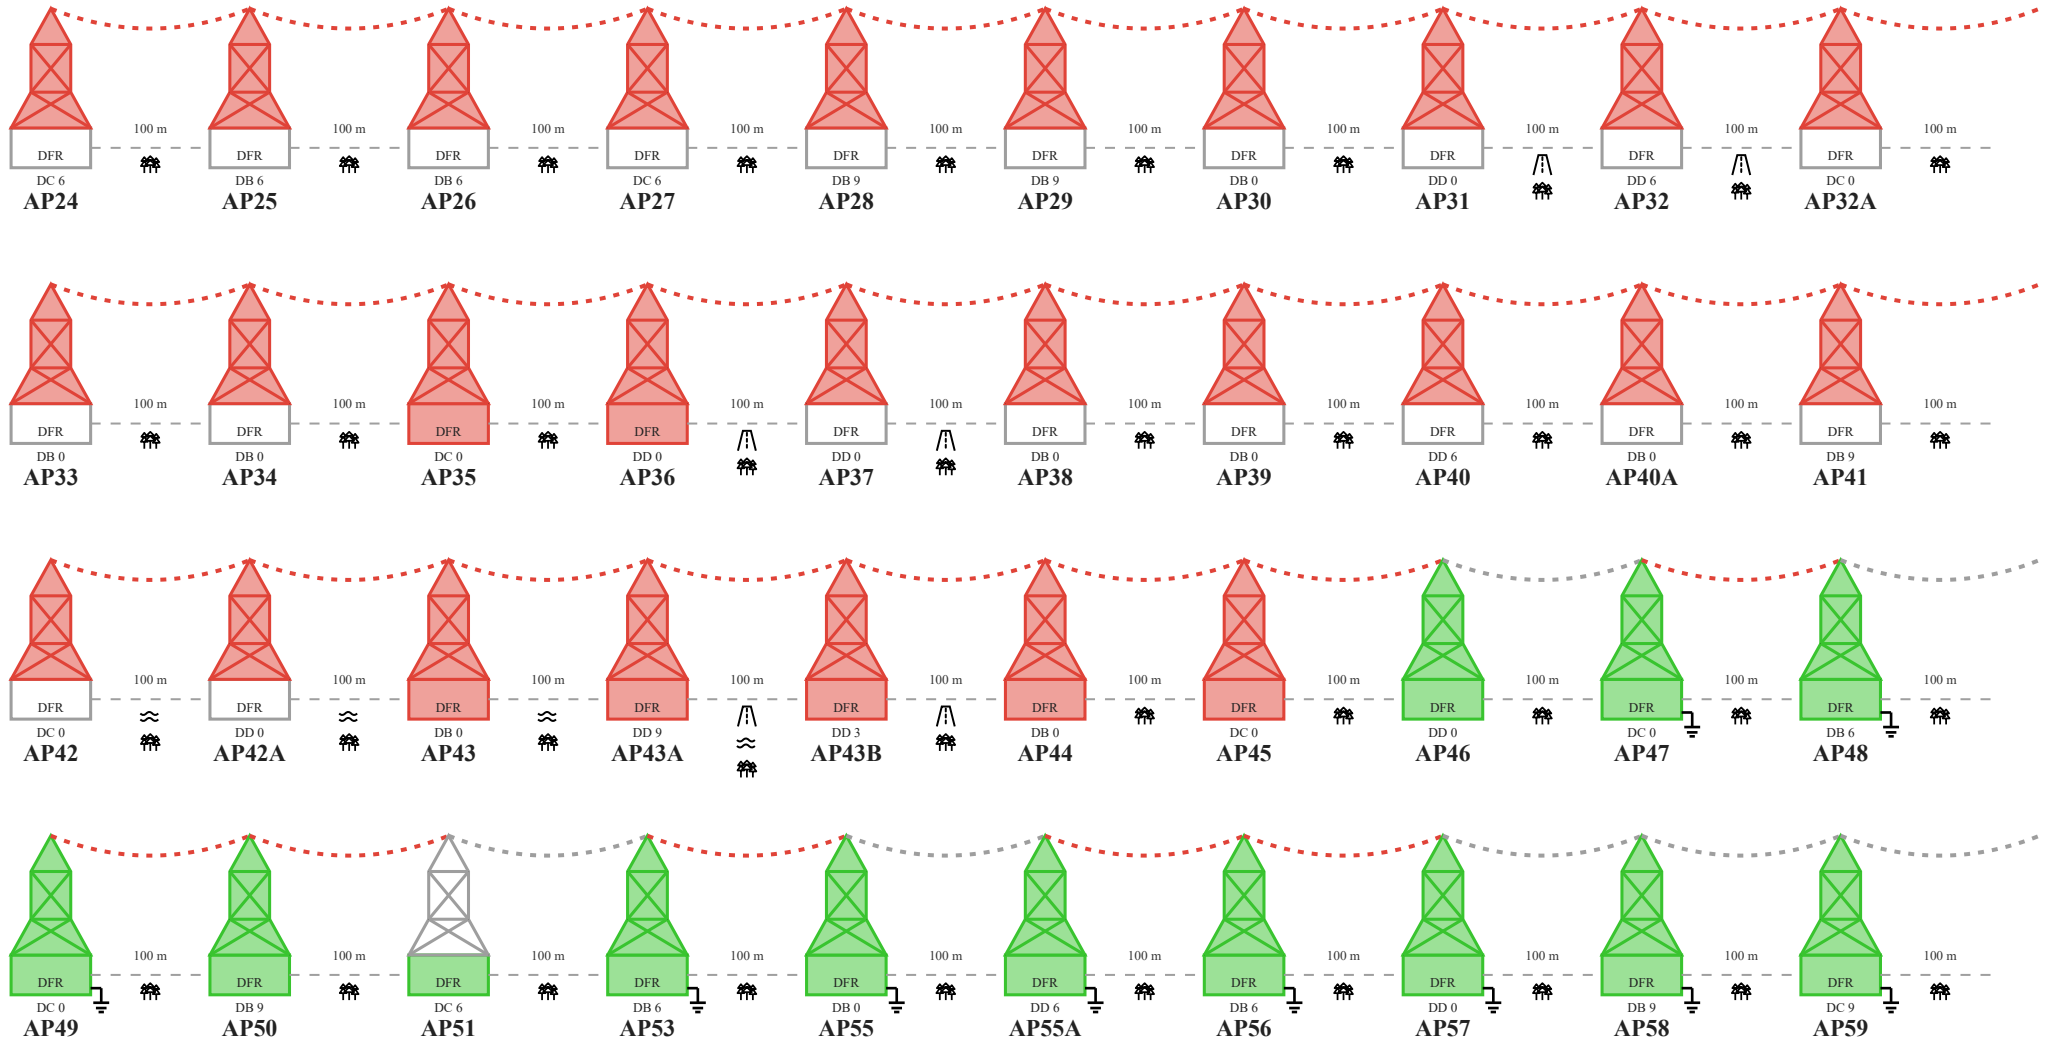

PROGRESS

Foundation	72 / 141
Erection	62 / 141
Earthing	59 / 141
Stringing	0.100 km / 15.709 km

132 kV S/C Rilo - Sagali TL


KEC INTERNATIONAL LTD.

Page 3 / 4 (Locations: AP60 to AP96A)

Progress data as on Wednesday, April 8, 2026

LEGEND

Crossings		Status	
	Road Crossing		Completed
	Rail Crossing		In Progress
	River Crossing		Right of Way
	Powerline Crossing		Planned
	Forest Crossing		Earthing Done

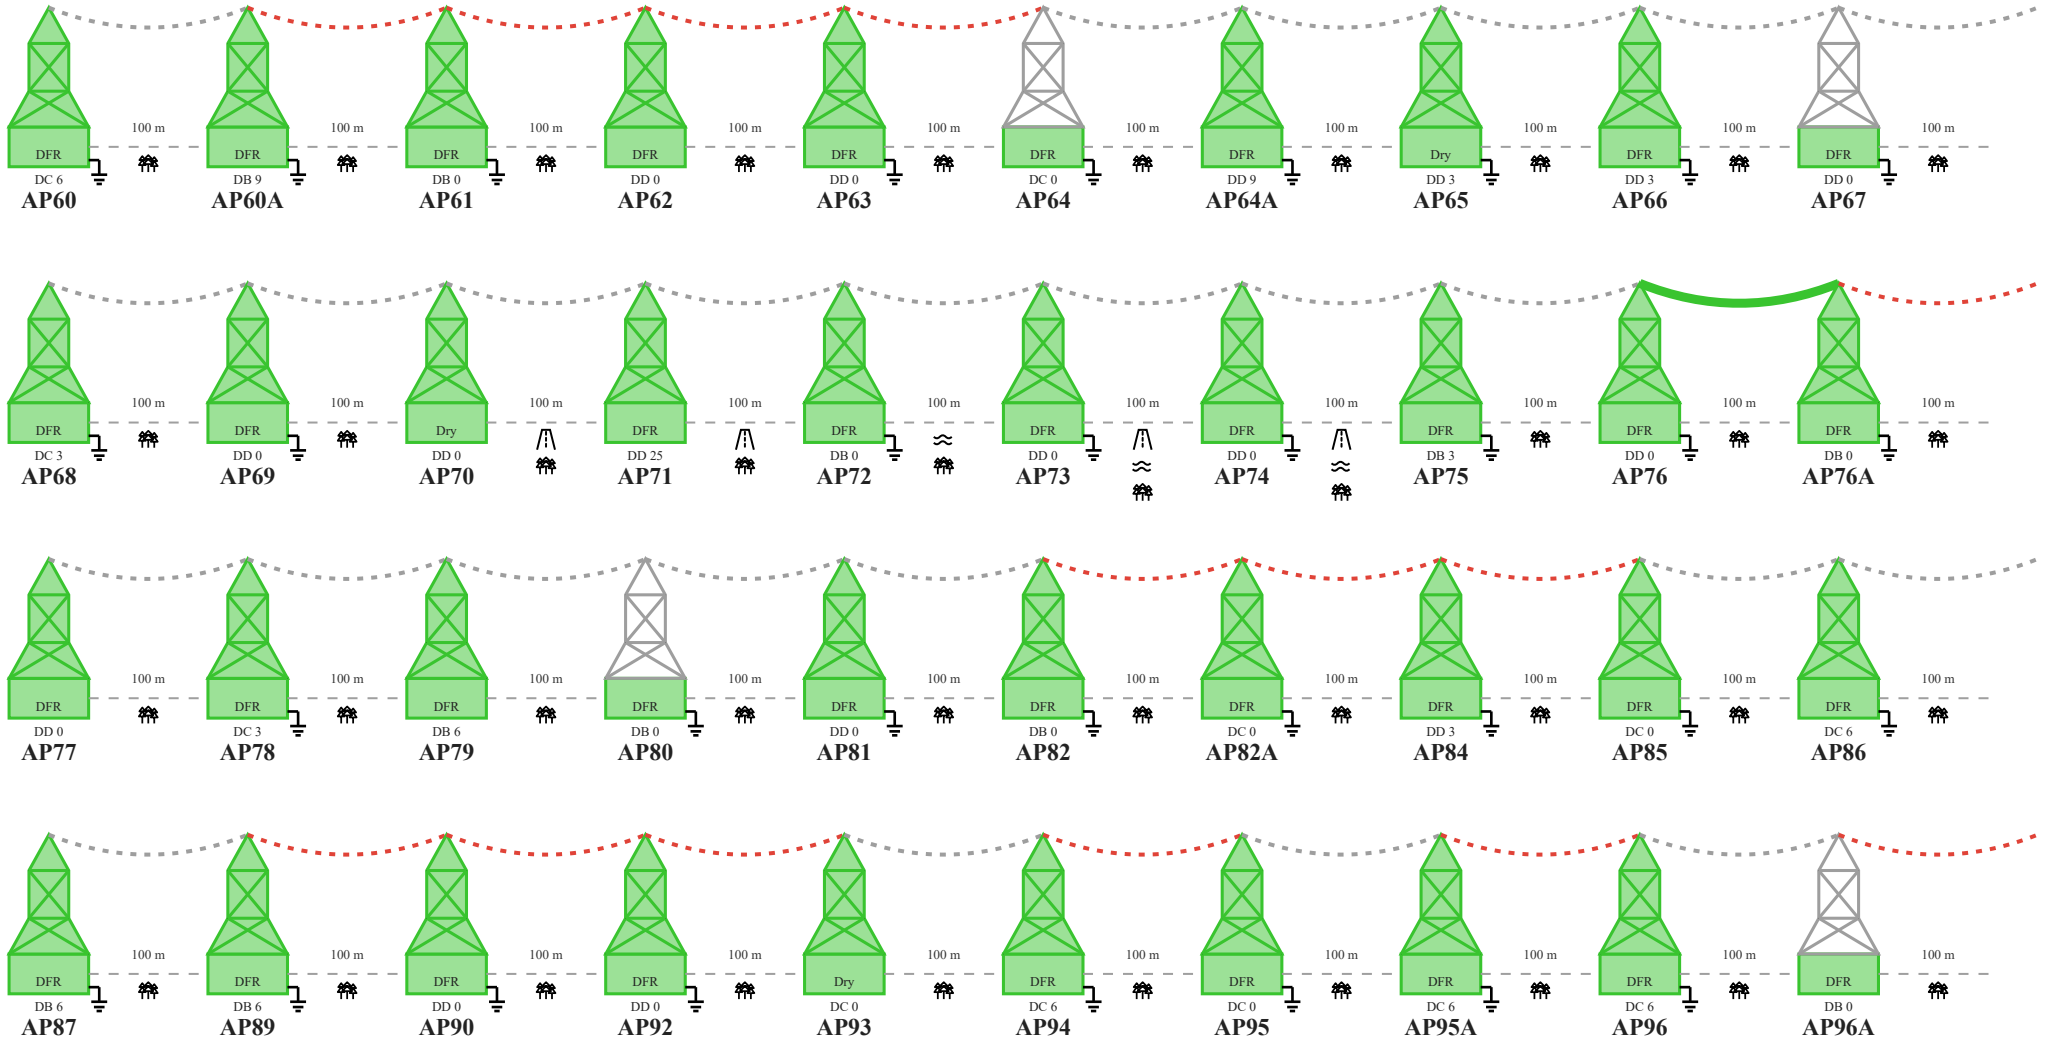

PROGRESS

Foundation	72 / 141
Erection	62 / 141
Earthing	59 / 141
Stringing	0.100 km / 15.709 km

132 kV S/C Rilo - Sagali TL

KEC INTERNATIONAL LTD.

Page 4 / 4 (Locations: AP97 to Sagalee)

Progress data as on Wednesday, April 8, 2026

LEGEND

Crossings		Status	
	Road Crossing		Completed
	Rail Crossing		In Progress
	River Crossing		Right of Way
	Powerline Crossing		Planned
	Forest Crossing		Earthing Done

